



MEMORANDUM
PUBLIC WORKS AND FACILITIES
ENGINEERING DIVISION
County of Placer

TO: Board of Supervisors
FROM: Ken Grehm, Director of Public Works and Facilities
By: Phil Vassion, Associate Civil Engineer
DATE: June 21, 2016
SUBJECT: Engineering / Notice of Completion / Auburn Folsom Road Class 2 Bike Lane Project, Contract No. 000924

ACTION REQUESTED

Adopt a Resolution accepting Construction Contract No. 000924 Auburn Folsom Road Class 2 Bike Lane Project as complete, and Authorize the Director of Public Works and Facilities, or designee, to execute a Notice of Completion.

BACKGROUND

This project installed a class 2 bike lane with separated concrete sidewalks on both sides of Auburn Folsom Road between Douglas Boulevard and Joe Rodgers Road.

The Board awarded Construction Contract No. 000924 to B&M Builders, Inc., on September 4, 2015 for \$649,129, and authorized the Director of Public Works to execute the contract and contract change orders up to an additional amount of \$100,000 for a total approval amount of \$749,129.

Work is complete at a cost of \$725,105. Filing a Notice of Completion establishes a deadline for anyone who wishes to make an additional claim on the project.

ENVIRONMENTAL IMPACT

A Categorical Exemption under CEQA was filed for the project on November 20, 2012 and a Categorical Exemption under NEPA was filed for the project on May 16, 2013.

FISCAL IMPACT

The final construction cost is \$725,105. Five (5) Contract Change Orders were issued for the project. A contract summary is attached. The project is funded through federal RSTP and CMAQ funding. The project was funded in the FY 2015-16 Final Budget, project Auburn Folsom Bikeway, PC2953.

ATTACHMENTS

Resolution
Notice of Completion
Contract Summary
Location Map

**Before the Board of Supervisors
County of Placer, State of California**

Resolution. No:.....

In the matter of: A resolution accepting the improvements as complete and authorizing the Director of Public Works and Facilities, or designee, to execute a Notice of Completion for the Auburn Folsom Road Class 2 Bike Lane Project, Contract No. 000924

The following Resolution was duly passed by the Board of Supervisors of the County of _____ at a regular meeting held _____, by the following

vote on roll call:

Ayes:

Noes:

Absent:

Signed and approved by me after its passage.

Chair, Board of Supervisors

Attest:

Clerk of said Board

BE IT RESOLVED by the Board of Supervisors, County of Placer, State of California, that this Board adopts this Resolution accepting the improvements as complete and authorizes the Director of Public Works and Facilities, or designee, to execute a Notice of Completion for the construction of the Auburn Folsom Road Class 2 Bike Lane Project, Contract No. 000924.

Name: AUBURN FOLSOM ROAD
CLASS 2 BIKE LANE PROJECT
Contract No.00924

Recording requested by: Kathy Henson
When recorded return to: Kathy Henson,
Placer County Department of Public Works

Exempt from Recording Fees – Govt. Code 27383

Space Above for Recorder

NOTICE OF COMPLETION

**COUNTY OF PLACER
DEPARTMENT OF PUBLIC WORKS AND FACILITIES
3091 County Center Drive, Suite 220
Auburn, CA 95603**

NOTICE IS HEREBY GIVEN, pursuant to California Civil Code Section 3093, that the following Contractor, to wit: Interstate Road Management, L.L.C., performed and completed, for the County of Placer, State of California, the following contract, roadway or work of improvement, to wit: Auburn Folsom Road Class 2 Bike lane Project.

The property is owned by the County of Placer _____ in fee _____

Said work was accepted on March 29, 2016

Executed this _____ day of _____, 2016, at Auburn, California. I declare under penalty of perjury that the foregoing is true and correct.

**KEN GREHM, DIRECTOR
DEPARTMENT OF PUBLIC WORKS, COUNTY OF PLACER**

A notary public or other officer completing this certificate verifies only the identity of the individual who signed the document to which this certificate is attached, and not the truthfulness, accuracy, or validity of that document.

**STATE OF CALIFORNIA)ss
COUNTY OF PLACER)**

On _____ before me JOHN P. WEBER, Notary Public, personally appeared **KEN GREHM**, who proved to me on the basis of satisfactory evidence to be the person whose name is subscribed to the within instrument and acknowledged to me that he executed the same in his authorized capacity, and that by his signature on the instrument the person, or the entity upon behalf of which the person acted, executed the instrument.

I certify under PENALTY OF PURJURY under the laws of the State of California that the foregoing paragraph is true and correct.

WITNESS my hand and official seal.

John P. Weber

MEMORANDUM

DEPARTMENT OF PUBLIC WORKS AND FACILITIES
County of Placer

TO: KEN GREHM

DATE: June 21, 2016

FROM: RICH MOOREHEAD

SUBJECT: NOTICE OF COMPLETION FOR THE AUBURN FOLSOM ROAD
CLASS 2 BIKE LANE PROJECT

Contractor: B&M Builders, Inc.

Work Completed: 3/29/16

Preliminary Estimate.....	\$	817,727.40
(1) Contract Award.....	\$	649,129.50
(2) Final Contract Cost:		
Completed Contract Items	\$	671,041.05
Contract Change Orders	\$	54,064.30
TOTAL	\$	<u>725,105.35</u>


Percent of Increase (Final Cost vs Contract Award)

(11.70%)


CCO #	Approved Cost	Description
1	\$968.83	Connect PVC drain pipe to new 18" CSP.
2	\$9,241.82	Revise sidewalk finish grades and wall heights from station 28+62.52 to 30+16.70. Add footing to back of walk.
3	\$5,000.00	Demo unsuitable rock at Cedar Oaks drive, replace waterline at driveway #9, remove EID patches in shoulders (west side), raise and reset sewer manhole at station 29+95 west side and reset 3 water valve lids for San Juan Water District.
4	\$5,274.48	Construct keystone retaining wall, west side, from station 30+62 to station 30+98.
5	\$33,579.17	Contract bid item overrun/adjustment for the following bid items: Construction Site Management, Traffic Control System, Portable CMS Boards, Radar Speed Trailer, Roadway Excavation
TOTAL	\$54,064.30	

AUBURN FOLSOM ROAD CLASS 2 BIKE LANE

VICINITY & LOCATION MAPS

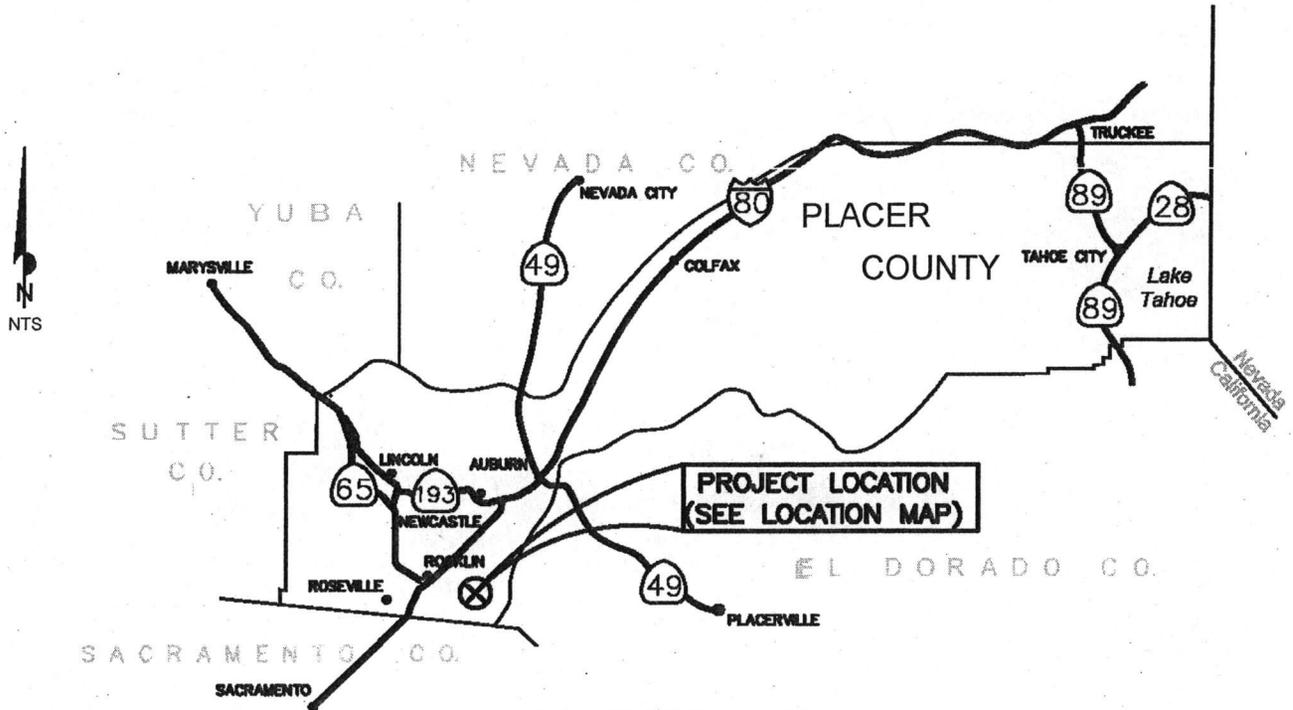

VICINITY MAP

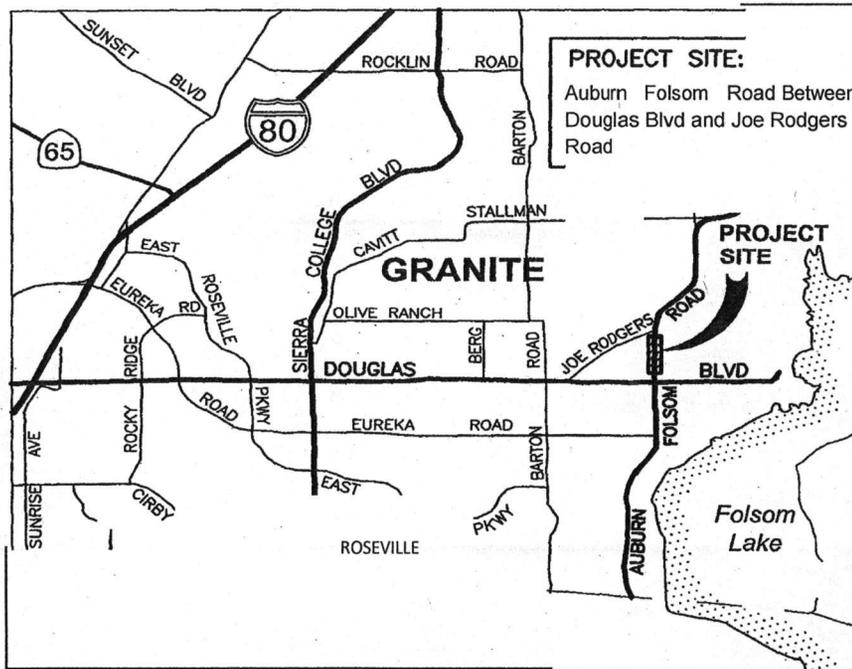

LOCATION MAP

NO SCALE
