

MEMORANDUM

DEPARTMENT OF PUBLIC WORKS
County of Placer

TO: BOARD OF SUPERVISORS

DATE: June 17, 2014

FROM: KEN GREHM / JEFF APPS

SUBJECT: COOK-RIOLO ROAD AT BASELINE ROAD SIGNAL MODIFICATION PROJECT –
CONTRACT NO. 1142 - NOTICE OF COMPLETION

ACTION REQUESTED / RECOMMENDATION

1. Adopt a Resolution for the Final Acceptance for the Cook-Riolo Road at Baseline Road Signal Modification Project.
2. Authorize the Director of Public Works to issue the Notice of Completion for the Cook-Riolo Road at Baseline Road Signal Modification Project as complete. There is no net County cost.

BACKGROUND / SUMMARY

On July 23, 2013, the Board of Supervisors awarded Construction Contract No. 1142 for the Cook-Riolo Road at Baseline Road Signal Modification Project to Biondi Paving and Engineering Inc. for \$192,589.00, and authorized the Director of Public Works to execute the contract and change orders up to ten percent for a total authorized amount of \$211,848.00. The Notice to Proceed was issued on August 5, 2013 and acceptance of the Final Pay Estimate (Invoice) was completed on May 22, 2014.

The project was located at the intersection of Cook-Riolo Road and Baseline Road, approximately 1.2 miles east of Fiddymont Road in Roseville (see Location Map).

Prior to project construction, vehicular traffic traveling north or south along Cook-Riolo Road/Woodcreek Oaks Blvd. was precluded at the intersection with Baseline Road by a concrete median diverter that forced them to turn left or right onto Baseline Road. The project removed the diverter, allowing all movements at the intersection. Removal of the diverter was approved by your Board on August 9, 2011 as part of an update to the Transportation/Circulation Element of the Dry Creek Community Plan.

ENVIRONMENTAL

This project was approved by the Placer County Board of Supervisors as part of the update to the Dry Creek Community Plan Transportation Element. The Final Environmental Impact Report was approved by the Placer County Planning Commission in October, 2010 and the Board of Supervisors on August 9, 2011.

FISCAL IMPACT

The final construction cost is \$202,547.75, which has been accepted by the Contractor with no exception. There were four (4) Contract Change Orders issued during project construction. A contract data and change order summary is attached as Exhibit A. Funding for the project is included in the FY 2013-14 Budget. The project was funded with local traffic impact fees from the Dry Creek Fee District with no net County cost.

Attachments: Resolution
Notice of Completion
Exhibit A – Contract Change Order Summary
Location Map

Before the Board of Supervisors County of Placer, State of California

In the matter of:

Resol. No: _____

ADOPT A RESOLUTION FOR THE FINAL ACCEPTANCE OF THE COOK RIOLO AT BASELINE ROAD SIGNAL MODIFICATION PROJECT AND AUTHORIZING THE DIRECTOR OF PUBLIC WORKS TO EXECUTE THE NOTICE OF COMPLETION FOR CONTRACT NO. 1142 THE COOK-RIOLO ROAD AT BASELINE ROAD SIGNAL MODIFICATION PROJECT

The following Resolution was duly passed by the Board of Supervisors of the County of Placer at a regular meeting held on _____ by the following vote on roll call:

Ayes:

Noes:

Absent:

Signed and approved by me after its passage.

Chair, Board of Supervisors

Attest:

Clerk of said Board

BE IT HEREBY RESOLVED by the Board of Supervisors of the County of Placer, State of California, that this Board accepts the construction Contract No.1142 as complete and authorizes the Director of Public Works to execute the Notice of Completion for the Cook-Riolo Road at Baseline Road Signal Modification Project completed by Biondi Paving and Engineering, Inc. for the amount of \$202,547.75.

Exhibit 'A'

MEMORANDUM

DEPARTMENT OF PUBLIC WORKS
County of Placer

TO: KEN GREHM DATE: June 17, 2014
FROM: RICHARD MOOREHEAD
SUBJECT: **NOTICE OF COMPLETION FOR COOK-RIOLO ROAD AT BASELINE
ROAD SIGNAL MODIFICATION PROJECT, CONTRACT NO. 1142
CONTRACT SUMMARY**


Contractor: Biondi Paving and Engineering
Work Completed: May 22, 2014

Preliminary Estimate.....	\$	178,965.00
(1) Contract Award.....	\$	192,589.00
(2) Final Contract Cost:		
Completed Contract Items	\$	192,239.00
Contract Change Orders	\$	10,308.75
Liquidated Damages	\$	(0.00)
TOTAL	\$	202,547.75


Percent of Increase (Final Contract Cost vs. Contract Award) 5.36 %

CONTRACT CHANGE ORDER SUMMARY:

CCO No.1	Relocation of Speed Humps	\$ 1,268.75
CCO No.2	Not Used	\$ 0.00
CCO No.3	Relocation of Vehicle Speed Feedback Sign	\$ 4,895.00
CCO No.4	Not Used	\$ 0.00
CCO No.5	Relocation of Pedestrian Button	\$ 1,155.00
CCO No.6	Concrete Pad and Truncated Domes	\$ 2,990.00
	Total	\$ 10,308.75

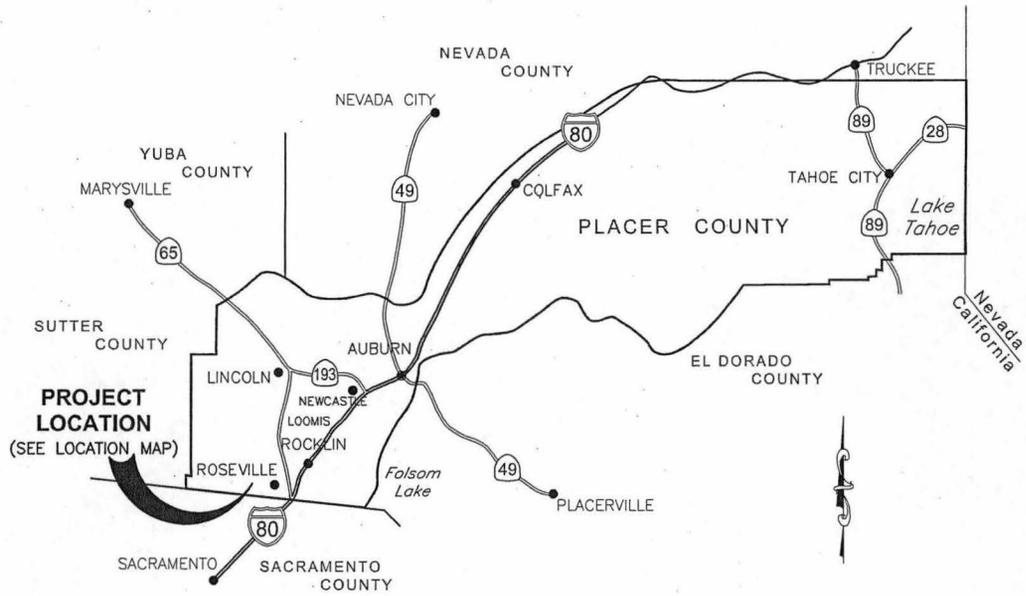

VICINITY MAP
NO SCALE

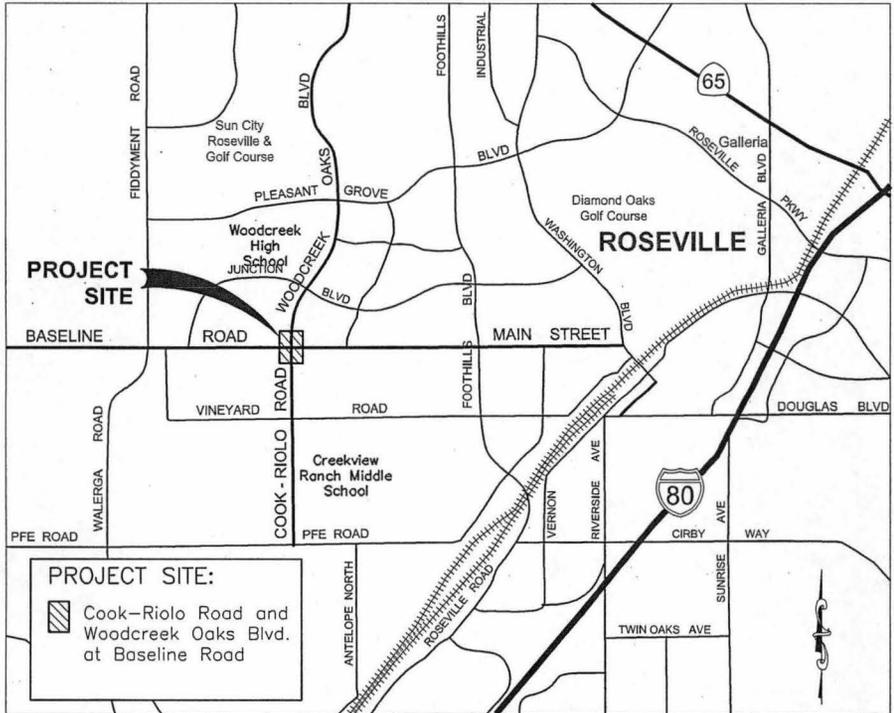

LOCATION MAP
NO SCALE

COOK RIOLO RD. AT BASELINE RD.
SIGNAL MODIFICATION PROJECT
Placer County, California

