



**MEMORANDUM  
PUBLIC WORKS  
ENGINEERING DIVISION**  
County of Placer

**TO:** Honorable Board of Supervisors **DATE:** July 12, 2022  
**FROM:** Ken Grehm, Director of Public Works  
**BY:** Jean Hanson, Associate Civil Engineer  
**SUBJECT:** Notice of Completion / Wise Road Over Doty Creek Bridge Replacement Project / Contract No. 000946

---

**ACTION REQUESTED**

Adopt a Resolution accepting the Wise Road over Doty Creek Bridge Replacement Project, Contract No. 000946 as complete, and authorize the Director of Public Works, or designee, to sign and record the Notice of Completion

**BACKGROUND**

The Department of Public Works, using Federal Highway Bridge Program Funds, replaced the one lane, narrow, 93 year old bridge on Wise Road over Doty Creek (Doty Ravine). The new bridge was constructed to current structural, geometric and hydraulic standards while maintaining the rural atmosphere and now provides safer mobility opportunities for vehicles, bicyclists, and pedestrians along Wise Road.

On March 7, 2017, your Board approved plans and specifications and authorized solicitation for bids for this project. On May 9, 2017, your Board awarded Construction Contract No. 000946 to the lowest responsive and responsible bidder, Steelhead Constructors, Inc. of Redding CA (SCI) in the amount of \$2,324,045 and authorized the Director of Public Works, or designee, to execute change orders up to \$232,405 as needed. Construction began shortly after award in the summer of 2017 and the new bridge was fully operational and open to traffic on December 5, 2017. SCI completed all punch list related items of work in the summer of 2018 and plant mitigation, monitoring and establishment was completed on April 7, 2022.

The contract was awarded for \$2,324,045 and the final cost is \$2,315,493. There were twelve (12) contract change orders issued during the project. A summary of construction costs and change orders is included as Attachment B.

**ENVIRONMENTAL IMPACT**

A Mitigated Negative Declaration under the California Environmental Quality Act (CEQA) with State Clearing House No. 2015032012 was adopted by your Board on May 5, 2015, and a NEPA Categorical Exclusion was approved by Caltrans on August 4, 2015, in compliance with the National Environmental Policy Act (NEPA) for the Wise Road over Doty Ravine Bridge Replacement Project.

**FISCAL IMPACT**

This action has no fiscal impact. The cost of this contract was included in the Department of Public Works FY 2017-18 through FY 2021-22 Budgets under line item PJ00511 Wise Road

Honorable Board of Supervisors

July 12, 2022

Notice of Completion / Wise Road Over Doty Creek Bridge Replacement Project / Contract No.  
000946

Page 2

over Doty Ravine Bridge Replacement project. This contract is fully funded by the Federal Highway Bridge Program (100%). There is no impact to the General Fund.

**ATTACHMENTS**

Attachment A - Resolution

Attachment B - Memorandum – Notice of Completion for the Wise Road over Doty Creek Bridge Replacement Project

Attachment C - Notice of Completion

Attachment D - Contract Change Order Summary

Attachment E - Location Map

Attachment A  
**Before the Board of Supervisors  
County of Placer, State of California**

**In the matter of:**

A Resolution accepting the Wise Road over Doty Ravine Bridge Replacement Project, Contract No. 000946 as complete, and authorizing the Director of Public Works, or designee, to sign and record the Notice of Completion.

Resolution No.: \_\_\_\_\_

The following Resolution was duly passed by the Board of Supervisors of the County of Placer at a regular meeting held on July 12, 2022, by the following vote:

Ayes:

Noes:

Absent:

Signed and approved by me after its passage.

\_\_\_\_\_  
Chair, Board of Supervisors

Attest:

\_\_\_\_\_  
Clerk of said Board

---

WHEREAS, the Wise Road over Doty Ravine bridge located in the City of Lincoln needed to be replaced; and

WHEREAS, on May 9th, 2017, the Board awarded Construction Contract No. 000946 to Steelhead Constructors, Inc., in the amount of \$2,324,045 and authorized the Director of Public Works, or designee, to execute change orders up to an amount of \$232,405 as needed; and

WHEREAS, construction of the bridge and all plant mitigation, monitoring and establishment was completed on April 7, 2022;

NOW, THEREFORE, BE IT RESOLVED, by the Board of Supervisors of the County of Placer, State of California, that this Board hereby accepts the Wise Road over Doty Ravine Bridge Replacement Project, Contract No. 000946 as complete, and authorizes the Director of Public Works, or designee, to sign and record the Notice of Completion.

**M E M O R A N D U M**

DEPARTMENT OF PUBLIC WORKS  
County of Placer

TO: KEN GREHM DATE: July 12, 2022  
FROM: JEAN HANSON  
SUBJECT: **NOTICE OF COMPLETION FOR THE WISE ROAD  
OVER DOTY RAVINE BRIDGE REPLACEMENT PROJECT**

---

Contractor: Steelhead Constructors, Inc.

Work Completed: April 7, 2022

Preliminary Estimate.....	\$	2,670,000.00
(1) Contract Award.....	\$	2,324,044.80
(2) Final Contract Cost:		
Completed Contract Items	\$	2,217,605.70
Contract Change Orders	\$	101,024.96
Administrative Deductions/Increases	\$	(3,137.50)
<b>TOTAL</b>	<b>\$</b>	<b>2,315,493.16</b>

Percent of Increase (Final Cost vs Contract Award) (0.37%)

Attachment C

Name: **WISE ROAD OVER DOTY CREEK  
BRIDGE REPLACEMENT PROJECT**

Contract No. 000946

Recording requested by: Danielle Williams  
When recorded return to: Danielle Williams,  
Placer County Department of Public Works  
3091 County Center Drive #220  
Auburn, CA 95603

Exempt from Recording Fees – Govt. Code 27383

**Space Above for Recorder**

---

**NOTICE OF COMPLETION**

**COUNTY OF PLACER  
DEPARTMENT OF PUBLIC WORKS  
3091 County Center Drive, Suite 220  
Auburn, CA 95603**

**NOTICE IS HEREBY GIVEN, pursuant to California Civil Code Section 3093, that the following Contractor, to wit: Steelhead Constructors, Inc., performed and completed, for the County of Placer, State of California, the following contract, work of improvement, to wit: Wise Road over Doty Ravine Bridge Replacement Project.**

The property is owned by the County of Placer.

Said work was completed and accepted on April 7, 2022

Executed this \_\_\_\_\_ day of \_\_\_\_\_ 2022, at Auburn, California. I declare under penalty of perjury that the foregoing is true and correct.

\_\_\_\_\_  
KEN GREHM, DIRECTOR  
DEPARTMENT OF PUBLIC WORKS, COUNTY OF PLACER

See Attached Notary Acknowledgement

Attachment D

**CONTRACT CHANGE ORDER SUMMARY**


Wise Road over Doty Creek Bridge Replacement Project  
 Contract No. 000946

<b>CCO#</b>	<b>DESCRIPTION</b>	<b>APPROVED COSTS</b>
01	Cofferdam Specification Change	\$ 0.00
02	Eliminate Field Office	\$ -
03	Provide Digital Design Model	\$ 0.00
04	Modify Soffit Detail	\$ 0.00
05	HMA Price Adjustment	\$ 4,392.80
06	Rock Removal at DS #6	\$ 3,116.29
07	Additional Tree Trimming and Drainage Ditch Cut	\$ 4,532.43
07-1	Fill ditch and Culvert Installation	\$ 14,351.61
07-2	Contract Time Adjustment - added 5 days	\$ 0.00
08	Eliminate Profilograph Requirement	\$ 0.00
09	Plants Relocation and Additional Plants Installation	\$ 2,181.49
09-1	Contract Time Adjustment - added 77 days	\$ 0.00
10	Drainage Inlet Lid Adjustment	\$ 16,711.94
10-1	Contract Time Adjustment - added 5 days	\$ 0.00
11	Potential Claim Number 1 Partial Resolution and return a portion of the administrative deduction	\$ 8,050.00
12	Potential Claim Numbers 1, 2 and 3 – Mutually Negotiated Global Settlement for All Potential and Actual Claims, Disputes and Damages	\$ 47,688.40
Total:		\$ 101,024.96


**PLACER COUNTY  
DEPARTMENT OF PUBLIC WORKS**

**WISE ROAD OVER DOTY CREEK BRIDGE REPLACEMENT PROJECT**

**LOCATION MAP**

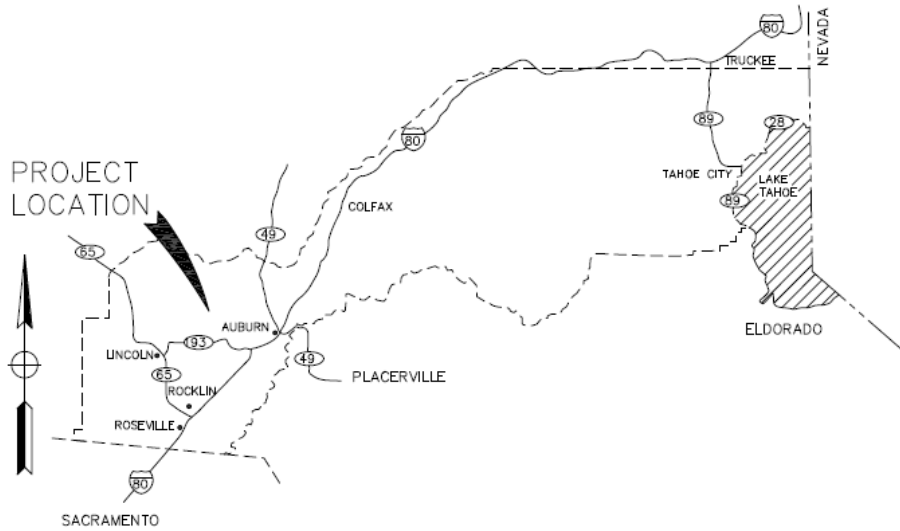

VICINITY MAP  
NO SCALE

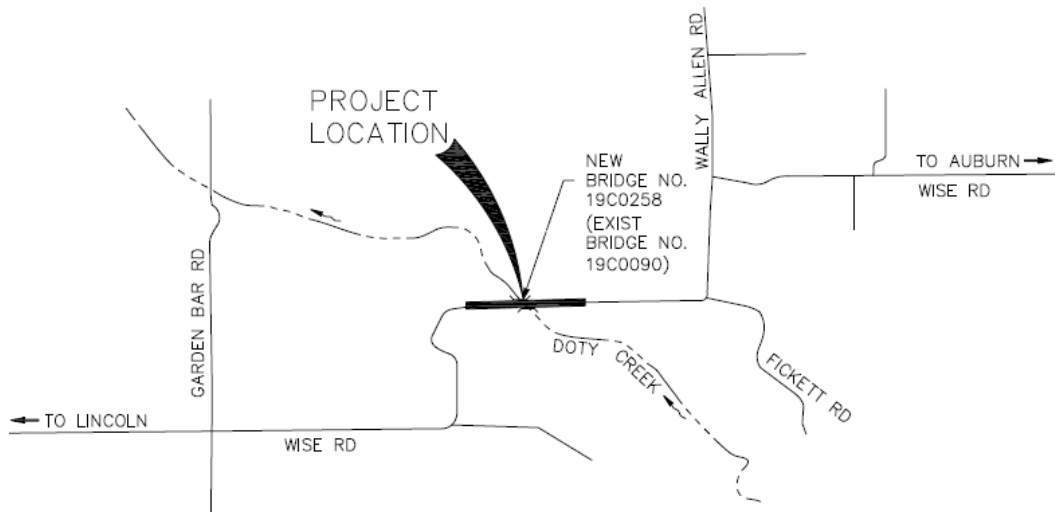

LOCATION MAP  
NO SCALE

