



**MEMORANDUM
PUBLIC WORKS
ENGINEERING DIVISION**
County of Placer

TO: Honorable Board of Supervisors **DATE:** September 27, 2022
FROM: Ken Grehm, Director of Public Works
BY: Kyle Friedrich, Associate Civil Engineer
SUBJECT: Notice of Completion / Dowd Road Over Raccoon Creek Bridge Replacement Project / Contract No. 001236

ACTION REQUESTED

Adopt a Resolution accepting the Dowd Road over Raccoon Creek Bridge Replacement Project, Contract No. 001236 as complete, and authorize the Director of Public Works, or designee, to sign and record the Notice of Completion.

BACKGROUND

The Department of Public Works, using Federal Highway Bridge Program Funds, replaced the narrow one-lane 83-year-old bridge on Dowd Road over Raccoon Creek. The new bridge was constructed to current structural, geometric and hydraulic standards and now provides safer multimodal means of transportation along Dowd Road.

On December 17, 2019, your Board approved plans and specifications and authorized solicitation for bids for this project. On April 27, 2021, your Board authorized the Director of Public Works, or designee to award and execute the construction contract to the lowest responsive and responsible bidder for an amount of \$5,413,560.50 and authorized the execution of change orders up to \$283,178.00. Eight bids were received and Viking Construction Inc. of Rancho Cordova, CA was the lowest responsive and responsible bidder. Construction of the bridge was completed and opened for public use on May 2, 2022.

The contract was awarded for \$5,413,560.50 and there were eight contract change orders issued during the project in the amount of \$137,290.92. The final cost is \$5,550,851.42.

ENVIRONMENTAL IMPACT

The Board approved the Initial Study/ Mitigated Negative Declaration (IS/MND) prepared for this project, pursuant to the California Environmental Quality Act (CEQA) with State Clearing House No. 2016082057 on October 25, 2016. A Categorical Exclusion Determination was approved by Caltrans on December 28, 2016, in compliance with the National Environmental Policy Act (NEPA).

FISCAL IMPACT

This action has no fiscal impact. The cost of this contract was included in the Department of Public Works FY 2020-2021 and FY 2021-2022 budgets under line item PJ00499 Dowd Road over Raccoon Bridge Replacement project. This contract is fully funded by the Federal Highway Bridge Program (100%).

Honorable Board of Supervisors

September 27, 2022

Notice of Completion / Dowd Road Over Raccoon Creek Bridge Replacement Project / Contract
No. 001236

Page 2

ATTACHMENTS

Attachment A - Resolution

Attachment B - Memorandum – Notice of Completion for the Dowd Road over Raccoon Creek
Bridge Replacement Project

Attachment C - Notice of Completion

Attachment D - Contract Change Order Summary

Attachment E - Location Map

Attachment A
Before the Board of Supervisors
County of Placer, State of California

In the matter of:

A Resolution accepting the Dowd Road over Raccoon Creek Bridge Replacement Project, Contract No. 001236 as complete, and authorizing the Director of Public Works, or designee, to sign and record the Notice of Completion.

Resolution No.: _____

The following Resolution was duly passed by the Board of Supervisors of the County of Placer at a regular meeting held on September 27, 2022, by the following vote:

Ayes:

Noes:

Absent:

Signed and approved by me after its passage.

Chair, Board of Supervisors

Attest:

Clerk of said Board

WHEREAS, the Dowd Road over Raccoon Creek bridge located West of the City of Lincoln needed to be replaced; and

WHEREAS, on April 27, 2021, the Board authorized the Director of Public Works, or designee to award and execute the construction contract to the lowest responsive and responsible bidder for an amount of \$5,413,560.50 and authorized the execution of change orders up to \$283,178; and

WHEREAS, eight bids were received and Viking Construction Inc. was the lowest responsible and responsive bidder and awarded Contract No. 001236 in the amount of \$5,413,560.50; and

WHEREAS, construction change orders totaled to \$137,290.92; and

WHEREAS, construction of the bridge was completed on May 2, 2022.

NOW, THEREFORE, BE IT RESOLVED, by the Board of Supervisors of the County of Placer, State of California, that this Board hereby accepts the Dowd Road over Raccoon Creek Bridge

Attachment A

Replacement Project, Contract No. 001236 as complete, and authorizes the Director of Public Works, or designee, to sign and record the Notice of Completion.

M E M O R A N D U M

DEPARTMENT OF PUBLIC WORKS
County of Placer

TO: KEN GREHM DATE: September 27, 2022
FROM: KYLE FRIEDRICH
SUBJECT: **NOTICE OF COMPLETION FOR THE DOWD ROAD
OVER RACCOON CREEK BRIDGE REPLACEMENT PROJECT**

Contractor: Viking Construction, Inc.

Work Completed: May 2, 2022

Preliminary Estimate.....	\$	3,243,000.00
(1) Contract Award.....	\$	5,413,560.50
(2) Final Contract Cost:		
Completed Contract Items	\$	5,413,560.50
Contract Change Orders	\$	137,290.92
Administrative Deductions/Increases	\$	0.00
TOTAL	\$	5,550,851.42

Percent of Increase (Final Cost vs Contract Award) (2.54%)

Attachment C

Name: **DOWD ROAD OVER RACCOON
CREEK BRIDGE REPLACEMENT PROJECT**

Contract No. 001236

Recording requested by: Danielle Williams
When recorded return to: Danielle Williams,
Placer County Department of Public Works
3091 County Center Drive #220
Auburn, CA 95603

Exempt from Recording Fees – Govt. Code 27383

Space Above for Recorder

NOTICE OF COMPLETION

**COUNTY OF PLACER
DEPARTMENT OF PUBLIC WORKS
3091 County Center Drive, Suite 220
Auburn, CA 95603**

NOTICE IS HEREBY GIVEN, pursuant to California Civil Code Section 3093, that the following Contractor, to wit: Viking Construction, Inc., performed and completed, for the County of Placer, State of California, the following contract, work of improvement, to wit: Dowd Road over Raccoon Creek Bridge Replacement Project.

The property is owned by the County of Placer.

Said work was completed and accepted on May 2, 2022

Executed this _____ day of _____ 2022, at Auburn, California. I declare under penalty of perjury that the foregoing is true and correct.

KEN GREHM, DIRECTOR
DEPARTMENT OF PUBLIC WORKS, COUNTY OF PLACER

See Attached Notary Acknowledgement

Attachment D

CONTRACT CHANGE ORDER SUMMARY

Dowd Road over Raccoon Creek Bridge Replacement Project
Contract No. 001236

CCO#	DESCRIPTION	APPROVED COSTS
01	Additional Traffic Control Device	\$ 5,000.00
02	Apprentice Training Reimbursement	\$ 2,800.00
03	Flood Event Additional SWPPP	\$ 8,601.00
04	Additional Grading	\$ 10,000.00
05	Modify Drainage System (G1 DI & Ditch)	\$ 75,000.00
06	Provide Additional RSP	\$ 1,900.58
07	Microsurfacing	\$ 16,957.50
08	Balancing Contract Change Order	\$ 3,932.17
		Total: \$ 137,290.92


**PLACER COUNTY
DEPARTMENT OF PUBLIC WORKS**

DOWD ROAD OVER RACCOON CREEK BRIDGE REPLACEMENT PROJECT

LOCATION MAP



VICINITY MAP

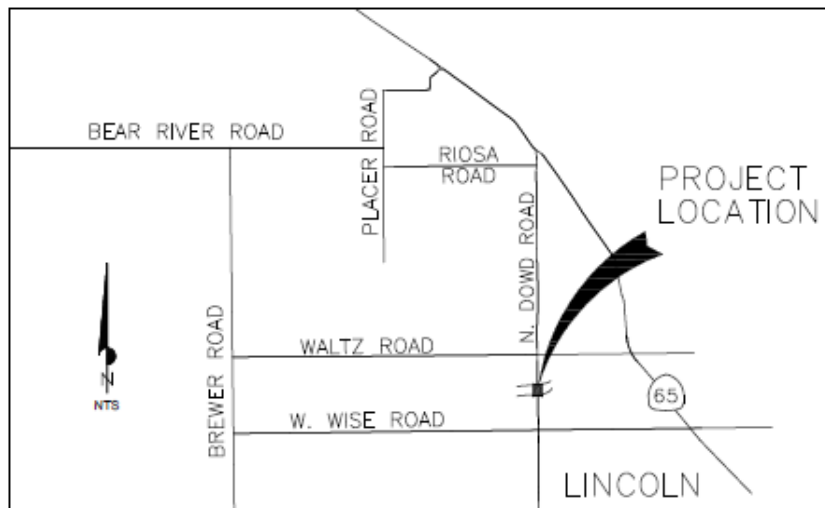

LOCATION MAP

NO SCALE
