

# MEMORANDUM

## DEPARTMENT OF PUBLIC WORKS

County of Placer

TO: BOARD OF SUPERVISORS  
DATE: January 11, 2011

FROM: KEN GREHM / PETER KRAATZ

SUBJECT: NOTICE OF COMPLETION FOR THE DONNER PASS ROAD STABILIZATION PROJECT, CONTRACT NO. 1099

### ACTION REQUESTED / RECOMMENDATION

Adopt a Resolution accepting the Donner Pass Road Stabilization Project as complete and approving and authorizing the Director of Public Works to execute the Notice of Completion for the Donner Pass Road Stabilization Project, Contract No 1099.

### BACKGROUND / SUMMARY

The Donner Pass Road Stabilization Project is located near the top of Donner Summit along Donner Pass Road across from Sugar Bowl Ski Area (see attached location map).

On June 22, 2010, the Board of Supervisors authorized the Department of Public Works to advertise for bids and allow the Public Works Director to execute a contract to construct a rock wall with vegetation, a rock channel, and a sedimentation basin. The contract was executed with Aspen Developers Corp. of Truckee, California on August 23, 2010, and work was completed on November 15, 2010.

### ENVIRONMENTAL

This project is categorically exempt from the provisions of CEQA under the following sections: Section 15307, Class 7; Section 15308, Class 8; and Section 15301(c), Class 1. A Notice of Exemption was posted with the County Clerk on November 7, 2007.

### FISCAL IMPACT

The contract was awarded for \$358,950 with a contingency of \$35,000. An additional \$50,000 was encumbered to cover work authorized by Contract Change Orders for a total of encumbrance of \$443,950. The final estimated cost of \$439,553 has been determined by this department. There were two Contract Change Orders issued during the project. A contract data and change order summary is attached as Exhibit A. The project is fully funded through erosion control grants from the Sierra Nevada Conservancy, Traffic Mitigation Funds, and California Tahoe Conservancy lease revenue. Funding for the construction of this project is included in the 2010-11 Fiscal Year Budget.

### Attachments:

Resolution  
Notice of Completion  
Location Map  
Exhibit A - Contract Summary Memo

Before the Board of Supervisors  
County of Placer, State of California

In the matter of: A RESOLUTION APPROVING  
AND AUTHORIZING THE DIRECTOR OF  
PUBLIC WORKS TO EXECUTE THE NOTICE  
OF COMPLETION FOR DONNER PASS ROAD  
STABILIZATION PROJECT, CONTRACT NO.  
1099

Resol. No:.....

Ord. No:.....

First Reading:.....

The following RESOLUTION was duly passed by the Board of Supervisors  
of the County of Placer at a regular meeting held \_\_\_\_\_,  
by the following vote on roll call:

Ayes:

Noes:

Absent:

Signed and approved by me after its passage.



\_\_\_\_\_  
Chairman, Board Of Supervisors

Attest:  
Clerk of said Board

\_\_\_\_\_  
\_\_\_\_\_  
BE IT HEREBY RESOLVED by the Board of Supervisors of the County of Placer, State  
of California, that this Board accepts the contract as complete and approving and  
authorizing the Director of Public Works to execute the Notice of Completion for the  
Donner Pass Road Stabilization Project, Contract No. 1099.

260



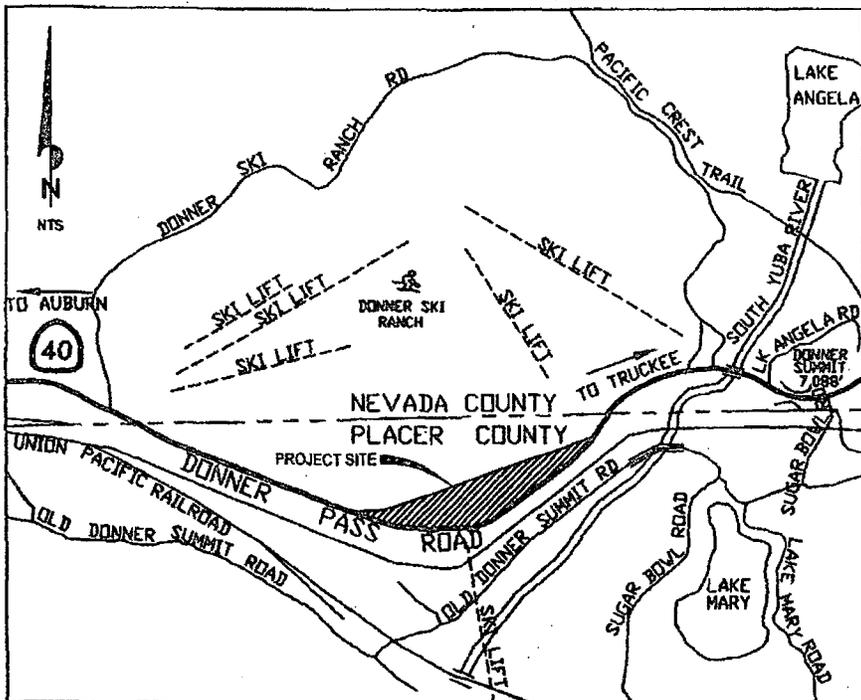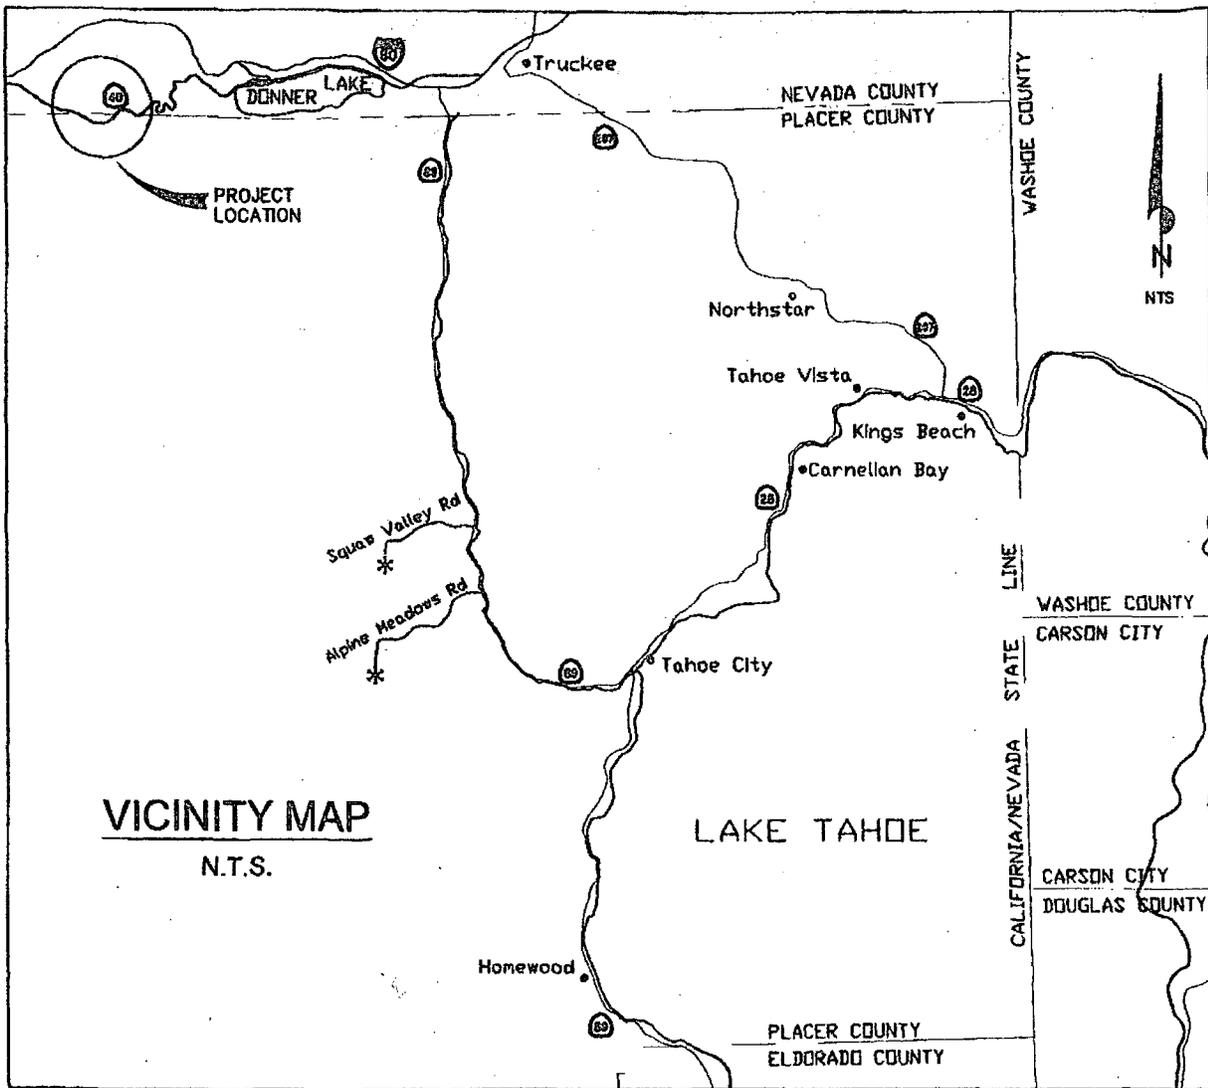

**PLACER COUNTY  
DEPARTMENT OF  
PUBLIC WORKS**

**Donner Pass Road  
Slope Rehabilitation**

**VICINITY & LOCATION MAP**

262

## MEMORANDUM

DEPARTMENT OF PUBLIC WORKS  
County of Placer

DATE: JANUARY 11, 2011  
TO: KEN GREHM  
FROM: GREG KEAVENEY  
SUBJECT: CONTRACT SUMMARY -- DONNER PASS ROAD STABILIZATION  
PROJECT, CONSTRUCTION CONTRACT NO. 1099

Contractor: Aspen Developers Corp.  
Work Completed: November 15, 2010

Preliminary Estimate	\$ 358,950
1. Contract Award	358,950
2. Estimated Final Contract Cost:	
--Completed Contract Items	360,212
--Contract Change Orders (CCOs)	79,341
	<hr/>
Total	\$ 439,553
Percent of increase (final contract versus contract award)	22.45

-----  
CONTRACT CHANGE ORDER SUMMARY

<u>CCO</u> <u>No.</u>	<u>Description</u>	<u>Net CCO Cost</u>
1.	Grading top hill	\$ 29,341
2.	Asphalt base, slope protection, and dirt removal	50,000
		<hr/>
	Total CCO Balance	\$ 79,341

