



**MEMORANDUM
PUBLIC WORKS
ENGINEERING DIVISION**
County of Placer

TO: Honorable Board of Supervisors **DATE:** December 7, 2021
FROM: Ken Grehm, Director of Public Works
BY: Kevin Ordway, Senior Civil Engineer
SUBJECT: Increase Construction Contract Change Order Authority / Contract No. 000993
– A. Teichert & Son, Inc. / Foresthill Road – Hilfiker Wall Stabilization Project

ACTION REQUESTED

Adopt a resolution authorizing the Director of Public Works, or designee, to execute a Construction Contract Change Order (CCO) to increase the limits of asphalt paving in an amount not to exceed \$105,000. This additional CCO authority will increase the total aggregate amount of CCO authority of the Director of Public Works, or designee, to \$181,586, consistent with Public Contract Code Section 20142 and the County Procurement Policy Manual. This action will increase the total contract amount not to exceed amount to \$1,461,711. This construction contract is funded with \$1,400,000 Federal Regional Surface Transportation Program funds and up to \$365,000 of Local Traffic Impact Fee funds.

BACKGROUND

In 2017, Placer County contracted with Crawford and Associates, Inc. to analyze the existing mechanically stabilized earth (MSE) wall on Foresthill Road. Their analysis confirmed that the wall was not compromised during the storms of 2016, but they identified some solutions for the localized pavement failure. Since this roadway is heavily utilized by Foresthill residents, the County has prioritized it for repair. The County has programmed Regional Surface Transportation Program (RSTP) funds and Local Road funds for construction.

On May 28, 2019, your Board approved the project plans and specifications and authorized the Director of Public Works, or designee, to advertise for construction bids. However, the project was delayed until all federal funds were authorized on September 4, 2020, which prevented construction until 2021.

On August 10, 2021, your Board approved the award of Contract No. 000993 to A. Teichert & Son, Inc. of Roseville, CA as the lowest responsive and responsible bidder with a total bid of \$1,281,711, for this project and authorized the Director of Public Works, or designee, to execute changes to the contract up to an amount of \$76,586, consistent with Public Contract Code Section 20142 and the County Procurement Policy. Construction is currently underway and is going well and the project is currently tracking to finish under budget. To minimize the cost of the project during design, an older segment of pavement was left in place between two separate sections of new pavement. However, the project has gone well and the Department would like to increase the limits of the asphalt overlay to provide for a seamless segment of new pavement and not leave an island of old pavement within the project limits. This action will provide for a total new segment of roadway within the current funding designated for the project.

Honorable Board of Supervisors

December 7, 2021

Increase Construction Contract Change Order Authority / Contract No. 000993 – A. Teichert & Son, Inc. / Foresthill Road – Hilfiker Wall Stabilization Project

Page 2

ENVIRONMENTAL IMPACT

The proposed project is exempt under CEQA pursuant to Guidelines, Class 1, Section 15301(c), Existing Facilities. A Categorical Exclusion Determination was approved by Caltrans on January 8th, 2019, in compliance with the National Environmental Policy Act (NEPA).

FISCAL IMPACT

The project is included in the Department of Public Works FY 2020-21 Budget under line item PJ00536, Hilfiker Wall Evaluation – Foresthill Road Project. The funding sources for the project include Regional Surface Transportation Program Funds and Local Road Funds. There is no net cost to the County. The total project cost is approximately \$2,000,000.

ATTACHMENTS

Resolution

Location Map

Before the Board of Supervisors County of Placer, State of California

In the matter of: A resolution authorizing the Director of Public Works, or designee, to execute a Construction Contract Change Order (CCO) to Contract No. 000993 with A. Teichert & Son, Inc., to increase the limits of asphalt paving in an amount not to exceed \$105,000. This additional CCO authority will increase the total aggregate amount of CCO authority of the Director of Public Works, or designee, to \$181,586, consistent with Public Contract Code Section 20142 and the County Procurement Policy.

Resolution No.: _____

The following Resolution was duly passed by the Board of Supervisors of the County of Placer at a regular meeting held December 07, 2021, by the following vote:

Ayes:

Noes:

Absent:


Signed and approved by me after its passage.

Chair, Board of Supervisors


Attest:

Clerk of said Board

BE IT RESOLVED, by the Board of Supervisors, County of Placer, State of California, that this Board approves the Resolution authorizing the Director of Public Works, or designee, to execute a Construction Contract Change Order (CCO) to Contract No. 000993 with A. Teichert & Son, Inc. of Roseville, CA, to increase to the limits of asphalt paving in an amount not to exceed \$105,000. This additional CCO authority will increase the total aggregate amount of CCO authority of the Director of Public Works, or designee, to \$181,586, consistent with Public Contract Code Section 20142 and the County Procurement Policy Manual.

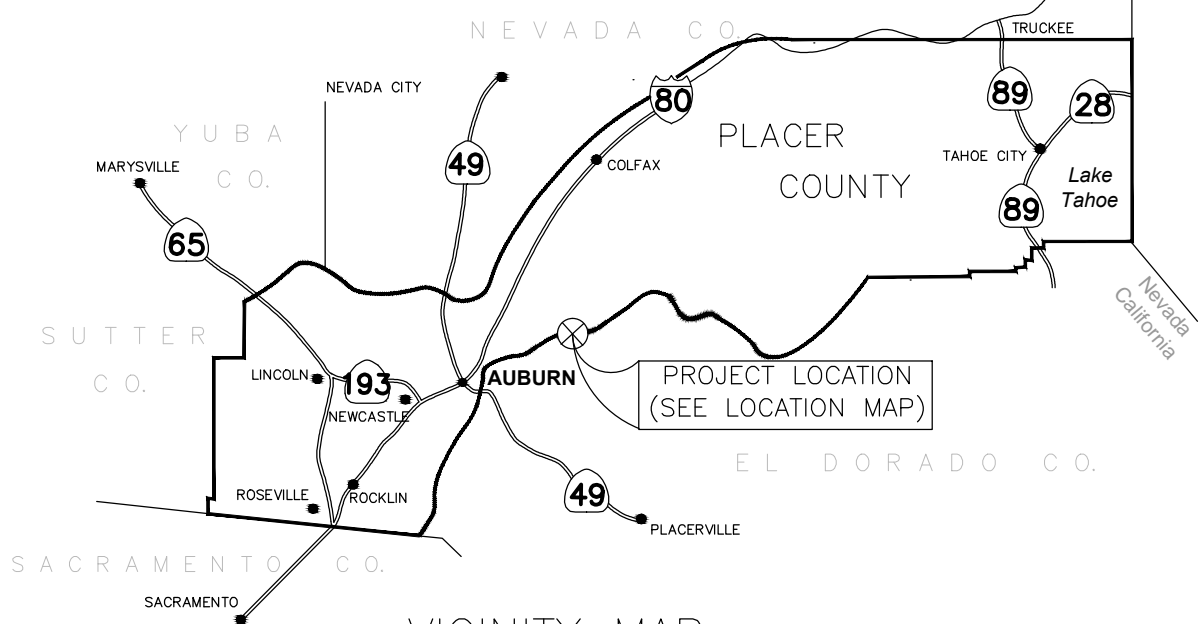

VICINITY MAP
NO SCALE

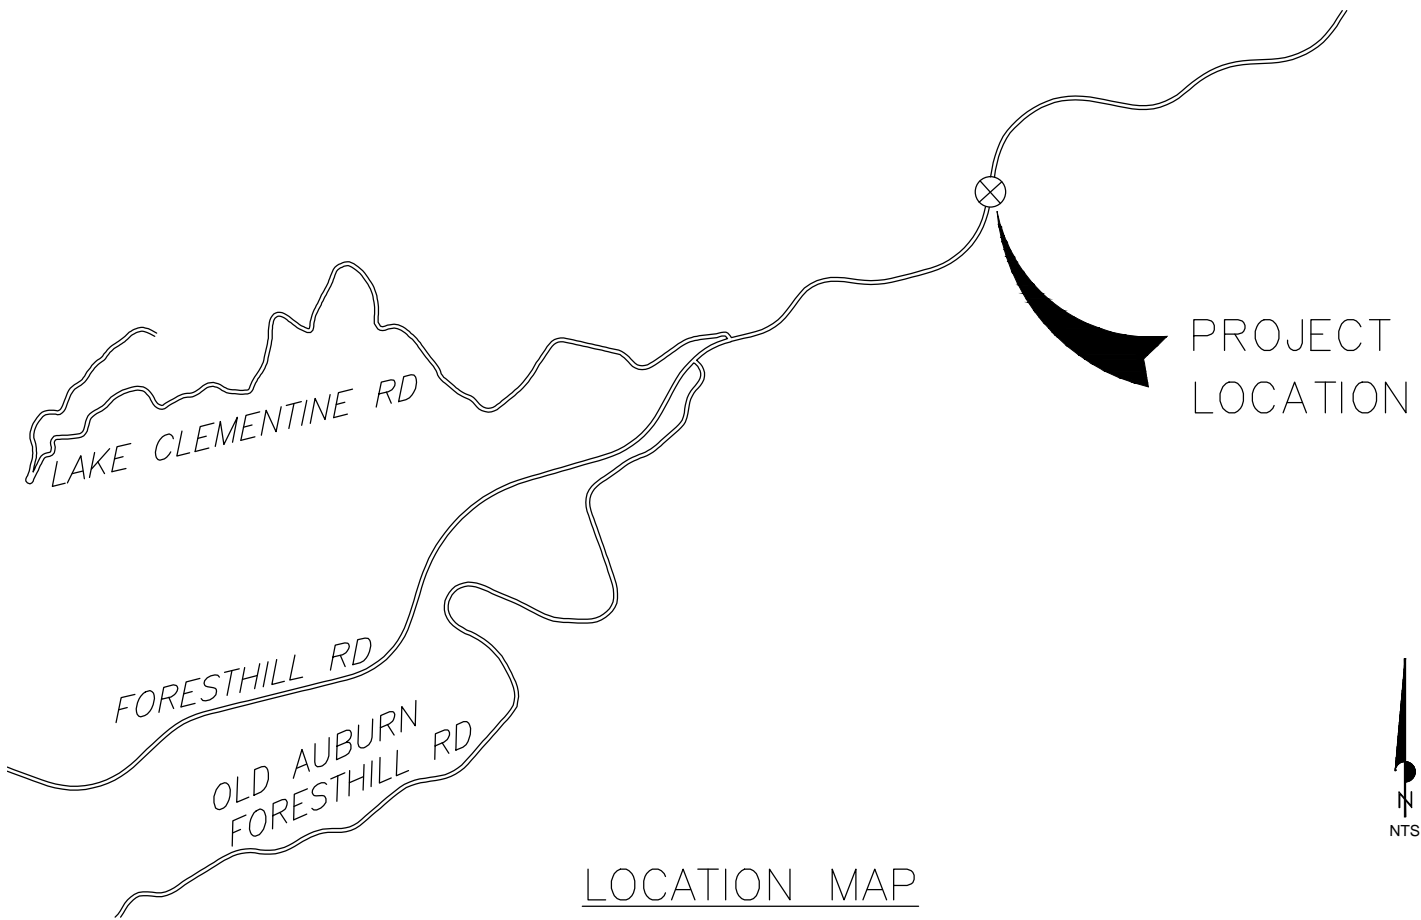

LOCATION MAP
NO SCALE

